



Name of the Work with Location:-	Repair/Renovation of Handicrafts office Complex, Janipur, Jammu
Department/Organization:-	Directorate of Handicrafts and Handloom, Jammu
Executing Agency:-	PW(R&B) Department
Block/District:-	Jammu(Janipur)
AA Cost (Rs. in Lakh):-	27.20 Lakh
Total Cost of Completion/Expenditure incurred ending 03/2022:-	17.20 Lakh /5.58 Lakh
Date of Start (Month/Year):-	03.12.2021
Date of Completion (Month/Year):-	03/2022



Name of the Work with Location:-	Up-gradation/repair and renovation of CFC at Omara, Udhampur
Department/Organization:-	Directorate of Handicrafts and Handloom, Jammu
Executing Agency:-	PW(R&B) Department
Block/District:-	Omara, Udhampur
AA Cost (Rs. in Lakh):-	20.48 Lakh
Total Cost of Completion/Expenditure incurred ending 03/2022:-	15.98 Lakh/15.98 Lakh
Date of Start (Month/Year):-	25.11.2019
Date of Completion (Month/Year):-	30.03.2022



Name of the Work with Location:-	Repair/Renovation of Handloom office Building Doda.
Department/Organization:-	Directorate of Handicrafts and Handloom, Jammu
Executing Agency:-	PW(R&B) Department
Block/District:-	Ghat/Doda
AA Cost (Rs. in Lakh):-	5.00 Lakh
Total Cost of Completion/Expenditure incurred ending 03/2022:-	5.00 Lakh/5.00 Lakh
Date of Start (Month/Year):-	09/2021
Date of Completion (Month/Year):-	02/2022







Latitude: 33.331732  
 Longitude: 75.764013  
 Elevation: 1620.08±3 m  
 Accuracy: 14.0 m  
 Azimuth: 131° (SE)  
 Pitch: -7.9° (3.6°)  
 Time: 16-04-2022 16:01  
 Note: Aluminium bifurcation of AD Handloom, Office Kishtwar.

Powered by AngleCam

Name of the Work with Location:-	Fabrication/Partitioning work of Handloom Office Building, Kisthwar.
Department/Organization:-	Directorate of Handicrafts and Handloom, Jammu
Executing Agency:-	PW(R&B) Department
Block/District:-	Kishtwar
AA Cost (Rs. in Lakh):-	5.00 Lakh
Total Cost of Completion/Expenditure incurred ending 03/2022:-	1.28 Lakh/1.28 Lakh
Date of Start (Month/Year):-	11/2021
Date of Completion (Month/Year):-	02/2022



Name of the Work with Location:-	Repair/renovation of CFC Budhi,Kathua.
Department/Organization:-	Directorate of Handicrafts and Handloom, Jammu
Executing Agency:-	PW(R&B) Department
Block/District:-	Budhi,Kathua
AA Cost (Rs. in Lakh):-	6.00 Lakh
Total Cost of Completion/Expenditure incurred ending 03/2022:-	4.06 Lakh/4.06 Lakh
Date of Start (Month/Year):-	11/2021
Date of Completion (Month/Year):-	02/2022



**Poonch, null, null**  
 Q39W+F33, Old City, Poonch, 185101  
 Lat 33.768821°  
 Long 74.09518°  
 18/04/22 12:11 PM


Name of the Work with Location:-	Repair/renovation of CFC/Handicrafts office Building, Haveli, Poonch.
Department/Organization:-	Directorate of Handicrafts and Handloom, Jammu
Executing Agency:-	PW(R&B) Department
Block/District:-	Haveli, Poonch
AA Cost (Rs. in Lakh):-	7.00 Lakh
Total Cost of Completion/Expenditure incurred ending 03/2022:-	6.70 Lakh/6.70 Lakh
Date of Start (Month/Year):-	04/2021
Date of Completion (Month/Year):-	03/2022

## Project-1 TOPA, POONCH

<b><u>Name of Work with</u></b> <b><u>Location:</u></b>	<b>Development/Fencing of New Industrial Estate Village Topa Tehsil Mankote Poonch (52 Kanal).</b>
<b>Department/Organization</b>	<b>Director Industries &amp; Commerce, Jammu</b>
<b>Executive Agency</b>	<b>SICOP</b>
<b>Block/District</b>	<b>TOPA, Tehs. Mankote (Distt. Poonch)</b>
<b>Estimated/Revised Cost</b> <b>(Rs. in Lakhs)</b>	<b>94.17 lakh</b>
<b>Allotment Cost</b>	<b>72.76 Lakh</b>
<b>Total Expenditure incurred</b> <b>(Rs. in Lakhs) on 03/2022</b>	<b>66.57 lakh</b>
<b>Project initiation Year</b>	<b>2020-21</b>
<b>Date of Completion</b>	<b>March, 2022</b>
<b>Physical Status</b>	<b>100% complete</b>




## Project-1 (TOPA)-Geo Tagged Image 1

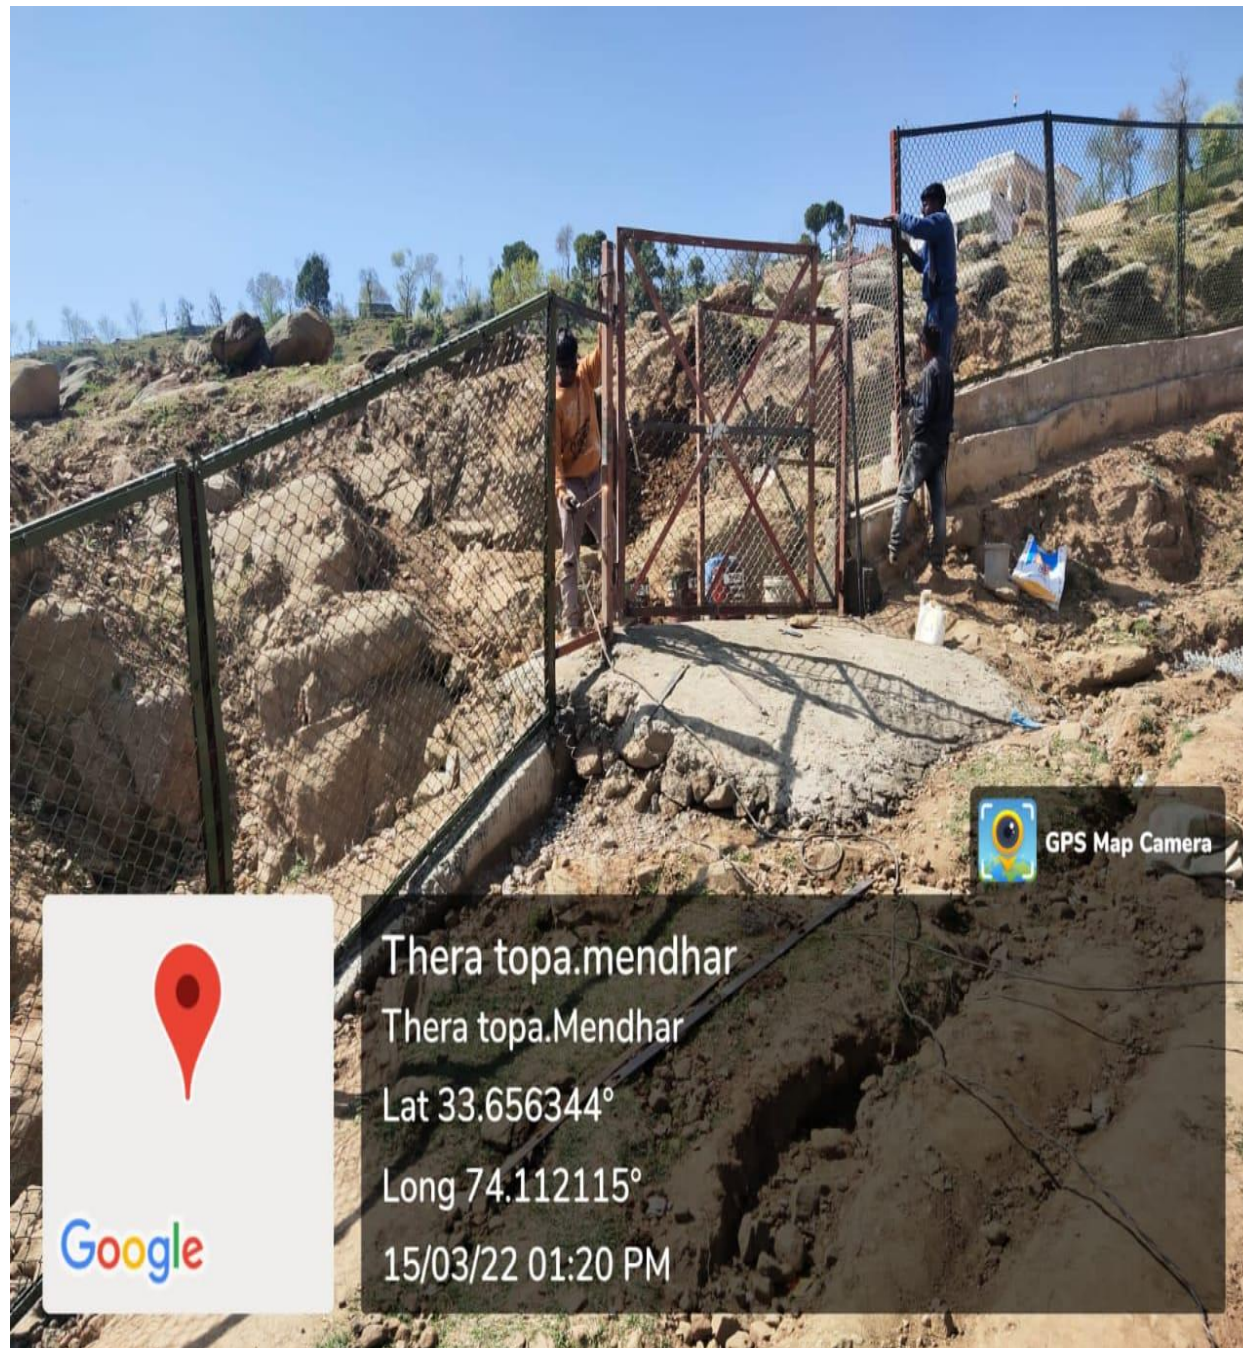




## Project-1 (TOPA)-Geo Tagged Image 2

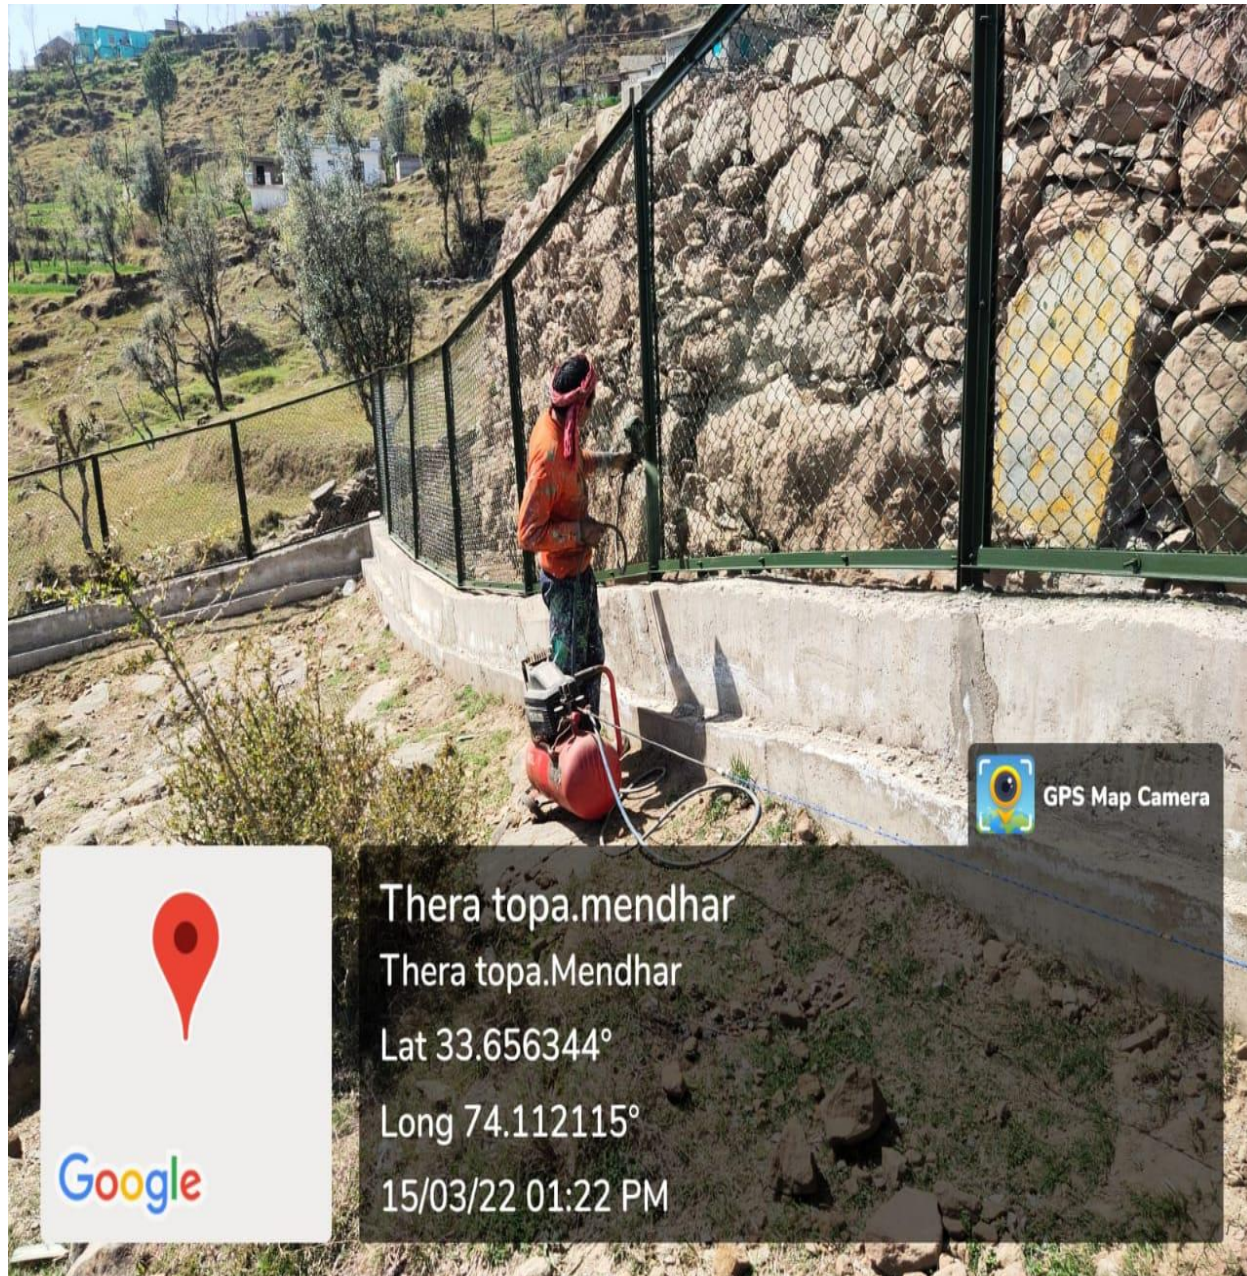



## Project-1 (TOPA)-Geo Tagged Image 3

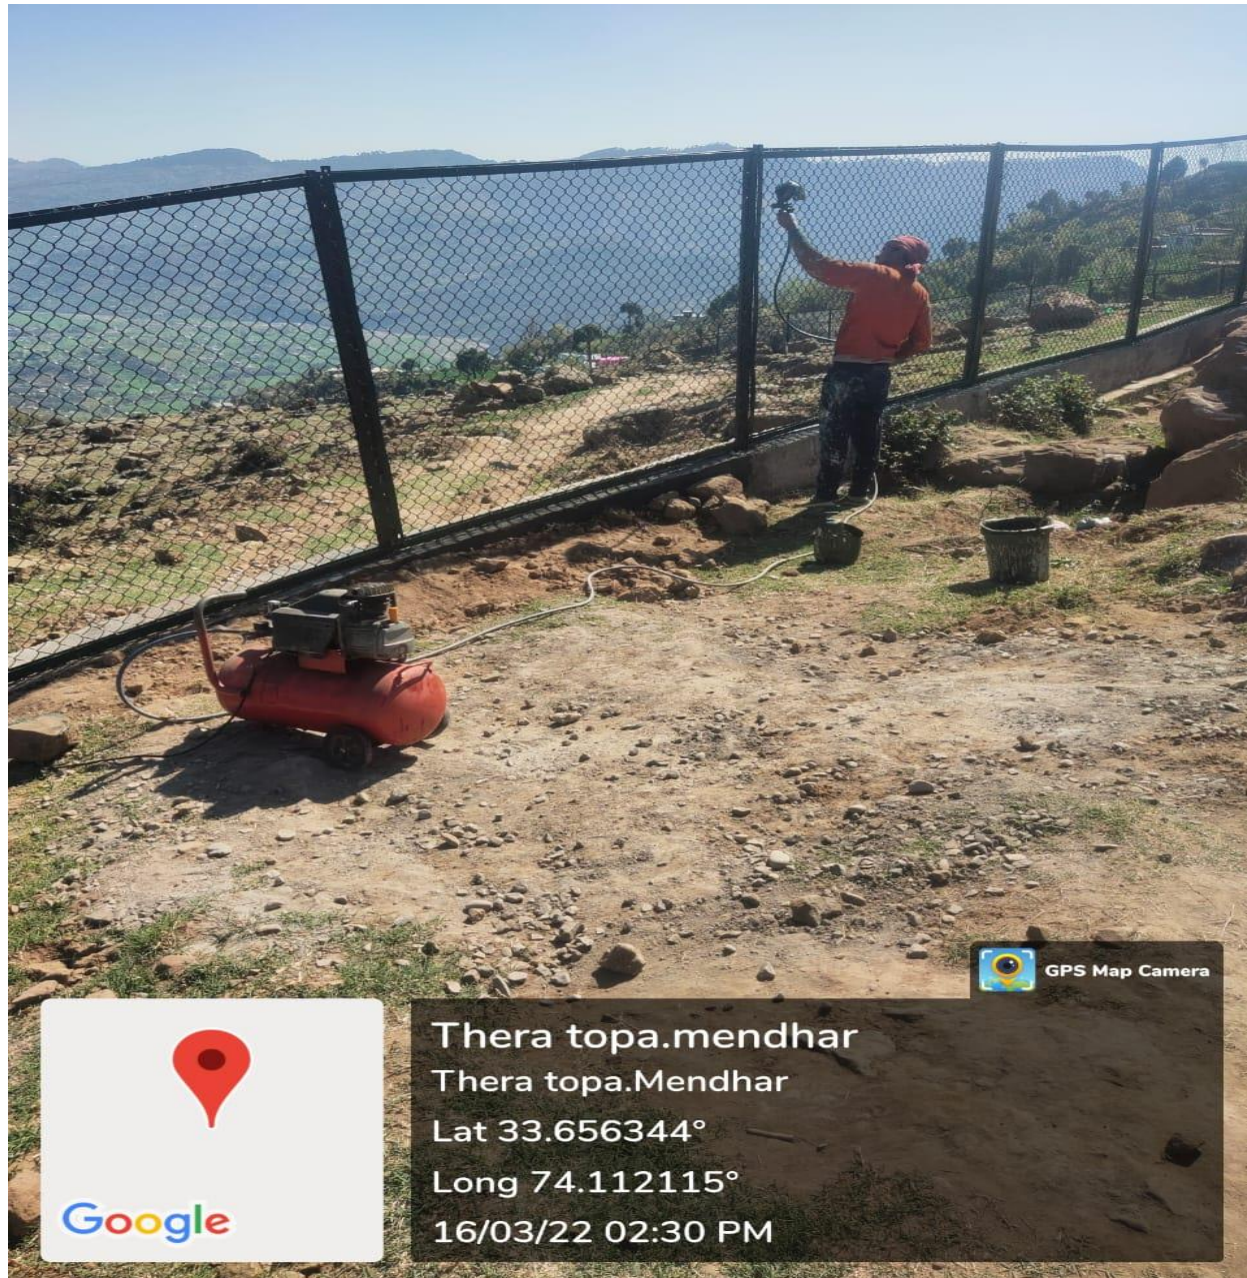

## Project-2 (DEHARI, UDHAMPUR)

<b><u>Name of Work with</u></b> <b><u>Location:</u></b>	<b>Providing and Fixing of Chain link fencing over plith fixed in steel frame at New Industrial Estate Village Dehari, Udhampur.</b>
<b>Department/Organization</b>	<b>Director Industries &amp; Commerce, Jammu</b>
<b>Executive Agency</b>	<b>SICOP</b>
<b>Block/District</b>	<b>Dehari, Ramnagar Distt. Udhampur.</b>
<b>Estimated/Revised Cost</b> <b>(Rs. in Lakhs)</b>	<b>397.10 lakh</b>
<b>Allotment Cost</b>	<b>225.68 Lakh</b>
<b>Total Expenditure incurred</b> <b>(Rs. in Lakhs) on 03/2022</b>	<b>150.00 lakh</b>
<b>Liability</b>	<b>75.68 Lakh (Projected under Capex 2022-23)</b>
<b>Project initiation Year</b>	<b>2020-21</b>
<b>Date of Completion</b>	<b>March, 2022</b>
<b>Physical Status</b>	<b>100% complete</b>



## Project-2 (DEHARI,UDHAMPUR)-Geo Tagged Image 1



Khein

Latitude

324625.086N

Longitude

03751528.008E

LOCAL 11:45:31

GMT 06:15:31

SATURDAY 04.16.2022

ALTITUDE 926 METER



## Project-2 (DEHARI,UDHAMPUR)-Geo Tagged Image 2





## Project-2 (DEHARI,UDHAMPUR)-Geo Tagged Image 3





<b>Format C</b> <b>Geo-tagged Photographs &amp; Details of works</b>	
Name of the work with location	Repair & Renovation of Assistant Director Handicrafts Kupwara office (including sales outlet/Showroom and Chowkidar residential hut)
Department/Organization	Directorate of Handicrafts & handloom Kashmir
Executive Agency	J&K SICOP
Block/District	Kupwara
AA Cost in lacs	61.68 lac
Total Cost of completion/ Expenditure incurred ending 03-2022	61.68lac
Date of start (Month/ Year)	18-03-2017
Date of completion (Month/ Year)	10-02-2022



<p><b>Format C</b></p> <p><b>Geo-tagged Photographs &amp; Details of works</b></p>	
Name of the work with location	Chain link fencing of District office Kupwara
Department/Organization	Directorate of Handicrafts & handloom Kashmir
Executive Agency	J&K SICOP
Block/District	Kupwara
AA Cost in lacs	8.18 lac
Total Cost of completion/ Expenditure incurred ending 03-2022	8.14 lac
Date of start (Month/ Year)	18-03-2017
Date of completion (Month/ Year)	15-02-202





**Format C**  
**Geo-tagged Photographs & Details of works**


Name of the work with location	Renovation of Electrification work of AD handicrafts Office at Kupwara
Department/Organization	Directorate of Handicrafts & handloom Kashmir
Executive Agency	J&K SICOP
Block/District	Kupwara
AA Cost in lacs	8.27 lac
Total Cost of completion/ Expenditure incurred ending 03-2022	7.55 lac
Date of start (Month/ Year)	10-03-2017
Date of completion (Month/ Year)	12-02-2022





**Geotagged Photograph (JPG format) with details Template enclosed.**

S. No.	Particulars	Status
1	Name of the work with location	Development of land, Boundary walling and allied works at Handicrafts office building Shopian
2	Department/ Organisation	Directorate of Handicrafts & Handloom Kashmir
3	Executive Agency	J&K SICOP
4	Block/District	Shopian
5	AA Cost (Rs. In Lakhs)	64.62
6	Total cost of Completion /expenditure incurred ending	64.00/ 50.00
7	Date of Start (Month /Year)	15.10.2020
8	Date of completion (Month /Year)	22.03 2022

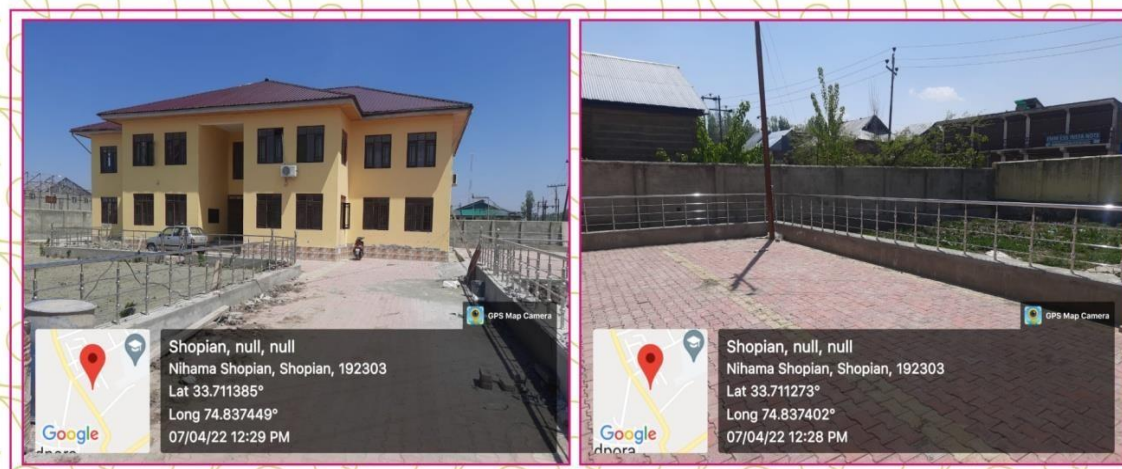

**Geotagged Photograph (JPG format) with details Template enclosed.**

S. No	Particulars	Status
1	Name of the work with location	Additional Works for reconstruction and electrification of Handicrafts Office Building at Shopian.
2	Department/ Organisation	Directorate of Handicrafts & Handloom Kashmir
3	Executive Agency	J&K SICOP
4	Block/District	Shopian
5	AA Cost (Rs. In Lakhs)	77.15
6	Total cost of Completion /expenditure incurred ending	77.00/ 66.50
7	Date of Start (Month /Year)	15.02.2020
9	Date of completion (Month /Year)	17.03.2022







Sr. No	2
Name of the work with Location	Installation of Solar lights in Kashmir Haat, srinagar
Department/Organisation	Directorate of Handicrafts & Handloom Kashmir
Exective Agency	J&K SICOP
Block/ District	Srinagar
AA Cost(Rs. In Lakhs)	24.480
Total Cost of Completion/ Expenditure incurred ending 3/2022	24.350
Date of start(Month/ Year)	24/09/2021
Date of completion (Month/ Year)	01/12/2021
No. of beneficiaries	



**Format "C"**  
**Geotagged Photograph(JPG format) with details**  
 Template enclosed

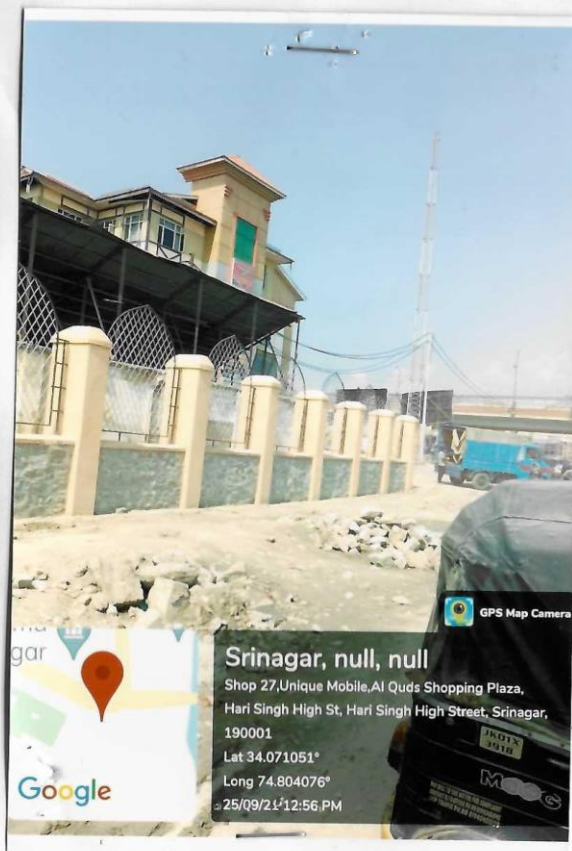

Sr. No	1
Name of the work with Location	Reconstruction of Walling to Kashmir Haat on Front Side of IG
Department/Organisation	Directorate of Handicrafts & Handloom Kashmir
Exective Agency	J&K SICOP
Block/ District	Srinagar
AA Cost(Rs. In Lakhs)	8.980
Total Cost of Completion/ Expenditure incurred ending 3/2022	7.725
Date of start(Month/ Year)	14/10/2021
Date of completion (Month/ Year)	20-02-2022
No. of beneficiaries	

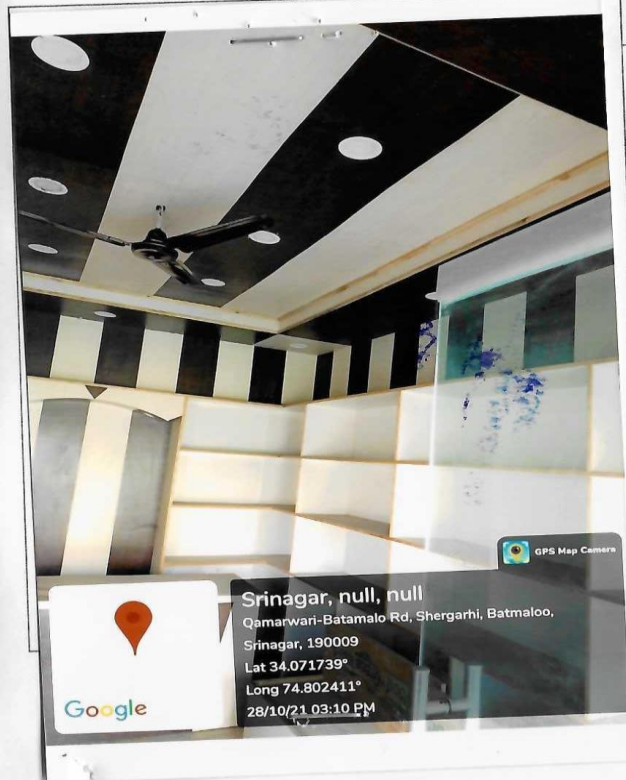


Sr. No	3
Name of the work with Location	Repair/ Renovation of Sales outlet at Kashmir Haat Srinagar
Department/Organisation	Directorate of Handicrafts & Handloom Kashmir
Exective Agency	J&K SICOP
Block/ District	Srinagar
AA Cost(Rs. In Lakhs)	4.500
Total Cost of Completion/ Expenditure incurred ending 3/2022	4.159
Date of start(Month/ Year)	18/03/2019
Date of completion (Month/ Year)	20/08/2021
No. of beneficiaries	



## Project-1 Development of IGC Lassipora

<b><u>Name of Work with</u></b> <b><u>Location:</u></b>	<b>Restoration of Flood Protection Bund at IGC Lassipora</b> <b>IGC Lassipora</b>
<b>Department/Organization</b>	<b>Director Industries &amp; Commerce, Kashmir</b>
<b>Executive Agency</b>	<b>SIDCO</b>
<b>Block/District</b>	<b>District Pulwama</b>
<b>Estimated/Revised Cost (Rs. in Lakhs)</b>	<b>Rs. 32.06 lakh</b>
<b>Total Expenditure incurred (Rs. in Lakhs) on 03/2022</b>	<b>Rs. 32.06 lakh</b>
<b>Project initiation Year</b>	<b>2020-21</b>
<b>Date of Completion</b>	<b>March, 2022</b>
<b>Physical Status</b>	<b>100% complete</b>

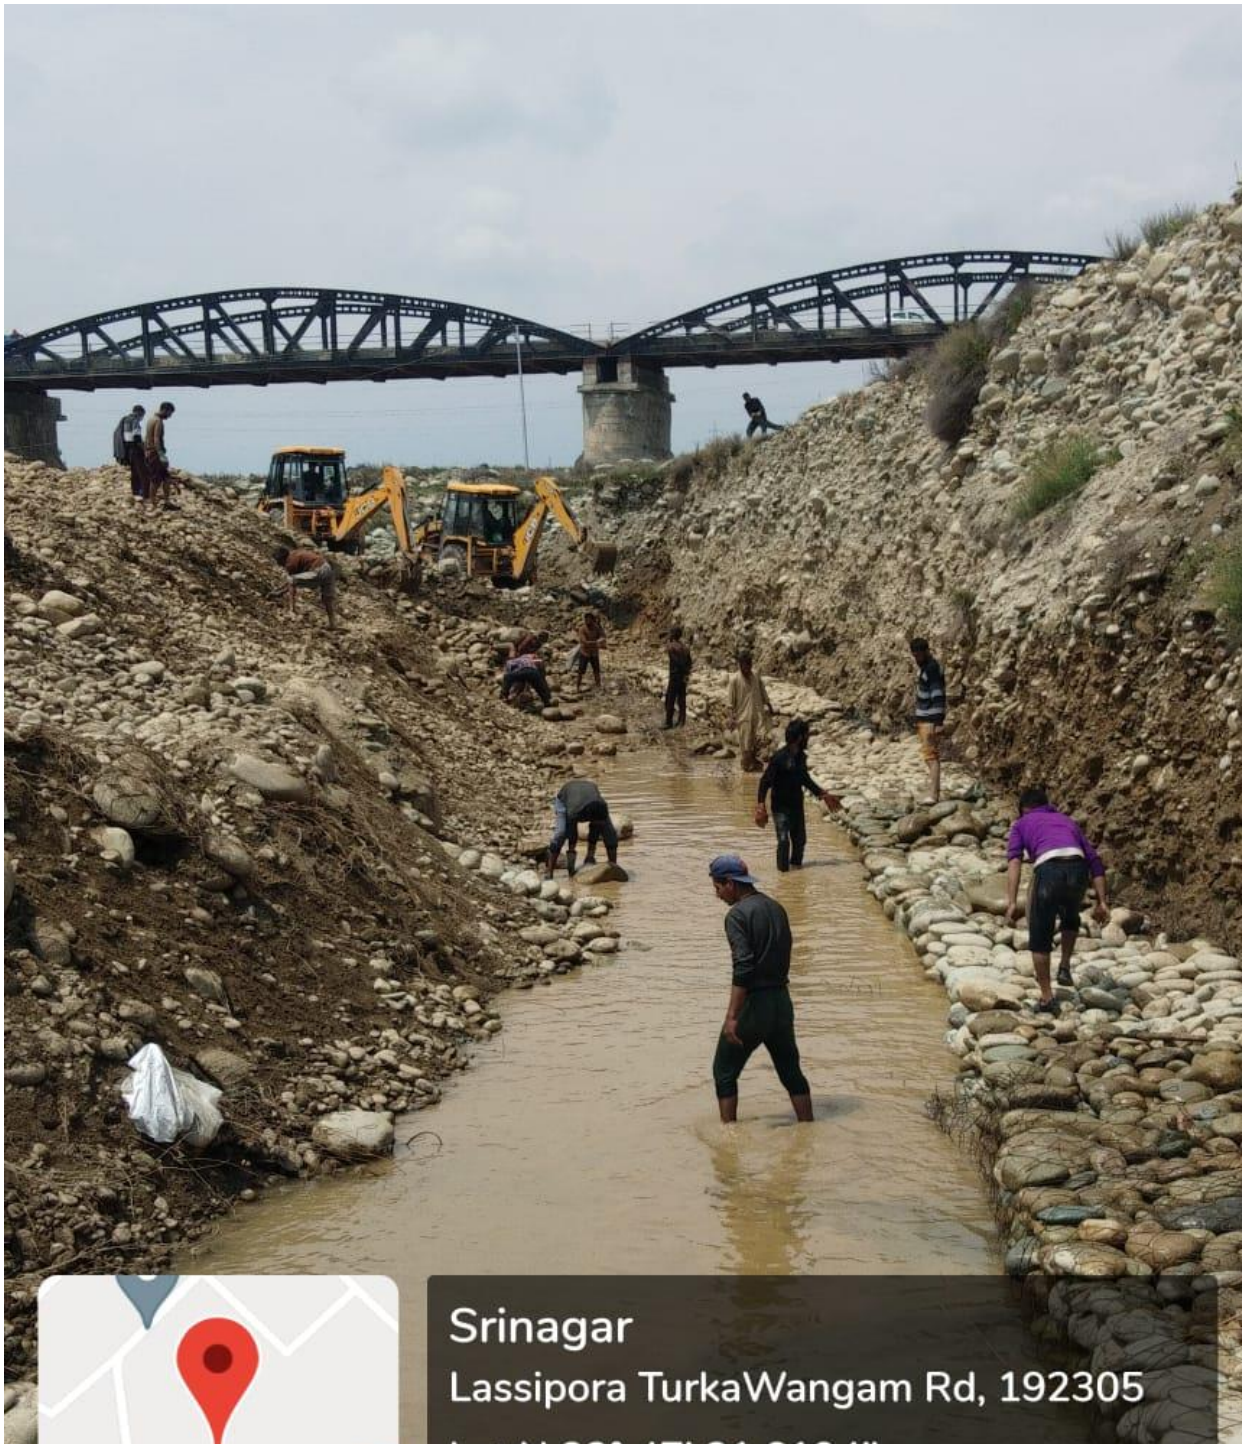

Srinagar  
Lassipora TurkaWangam Rd, 192305



## Project-1 Development of IGC Lassipora

<b><u>Name of Work with</u></b> <b><u>Location:</u></b>	<b>Channelization of Ranbir Nallah on D/Stream side of the bridge IGC Lassipora</b> <b>IGC Lassipora</b>
<b>Department/Organization</b>	<b>Director Industries &amp; Commerce, Kashmir</b>
<b>Executive Agency</b>	<b>SIDCO</b>
<b>Block/District</b>	<b>District Pulwama</b>
<b>Estimated/Revised Cost (Rs. in Lakhs)</b>	<b>Rs. 6.76 lakh</b>
<b>Total Expenditure incurred (Rs. in Lakhs) on 03/2022</b>	<b>Rs. 6.76 lakh</b>
<b>Project initiation Year</b>	<b>2020-21</b>
<b>Date of Completion</b>	<b>November, 2021</b>
<b>Physical Status</b>	<b>100% complete</b>



Lassipora TurkaWangam Rd, 192305

Latitude

Longitude



## Project-1 Development of IGC Lassipora

<b><u>Name of Work with</u></b> <b><u>Location:</u></b>	<b>Construction of RCC Culvert near M/S Mir agro at IGC Lassipora</b> <b>IGC Lassipora</b>
<b>Department/Organization</b>	<b>Director Industries &amp; Commerce, Kashmir</b>
<b>Executive Agency</b>	<b>SIDCO</b>
<b>Block/District</b>	<b>District Pulwama</b>
<b>Estimated/Revised Cost (Rs. in Lakhs)</b>	<b>Rs. 39.08 lakh</b>
<b>Total Expenditure incurred (Rs. in Lakhs) on 03/2022</b>	<b>Rs. 39.08 lakh</b>
<b>Project initiation Year</b>	<b>2020-21</b>
<b>Date of Completion</b>	<b>March, 2022</b>
<b>Physical Status</b>	<b>100% complete</b>



Unnamed Road, 192305

Latitude  
33.80932251°

Longitude  
74.93573293°





## Project-2 Macadamization of road at IGC Lassipora

<b><u>Name of Work with</u></b>	<b>Macadamization of Main Spine Road at IGC Lassipora</b>
<b><u>Location:</u></b>	<b>IGC Lassipora</b>
<b>Department/Organization</b>	<b>Director Industries &amp; Commerce, Kashmir</b>
<b>Executive Agency</b>	<b>SIDCO</b>
<b>Block/District</b>	<b>District Pulwama</b>
<b>Estimated/Revised Cost (Rs. in Lakhs)</b>	<b>Rs. 100.00 lakh</b>
<b>Total Expenditure incurred (Rs. in Lakhs) on 03/2022</b>	<b>Rs. 37.50 lakh</b>
<b>Project initiation Year</b>	<b>2020-21</b>
<b>Date of Completion</b>	<b>March, 2022</b>
<b>Physical Status</b>	<b>100% complete physically but financially under progress</b>






Unnamed Road, 192305

Latitude

Longitude

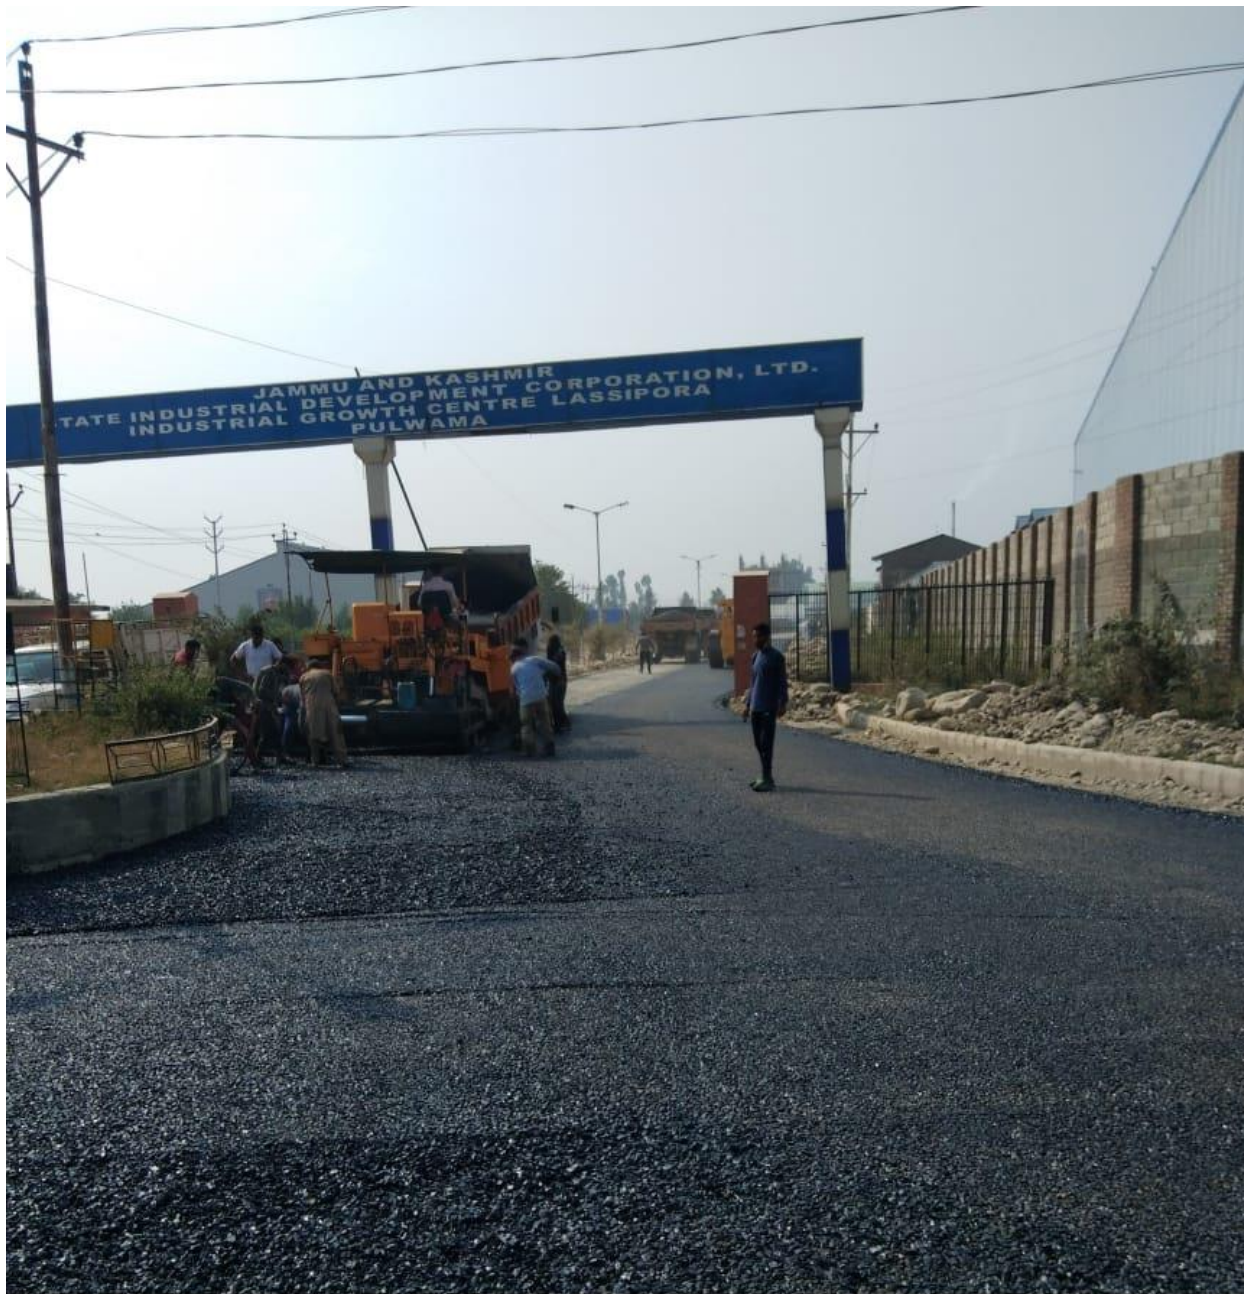

Unnamed Road, 192305

Latitude

Longitude





Unnamed Road, 192305

Latitude

Longitude

## **Project-3Repair/Renovation at DIC Office, Srinagar.**

<b><u>Name of Work with</u></b>	<b>Renovation of Strong Room cum Record room on ground floor and wooden paneling of Record room/ Accounts Section room/ EI Section room including electrification at IE BAMK, DIC Office Srinagar</b>
<b>Location</b>	<b>Industrial Estate, BAMK Srinagar</b>
<b>Department/Organization</b>	<b>Director Industries &amp; Commerce, Kashmir</b>
<b>Executive Agency</b>	<b>SICOP</b>
<b>Block/District</b>	<b>District Srinagar</b>
<b>Estimated/Revised Cost (Rs. in Lakhs)</b>	<b>Rs. 13.30 lakh</b>
<b>Total Expenditure incurred (Rs. in Lakhs) on 03/2022</b>	<b>Rs. 13.23 lakh</b>
<b>Project initiation Year</b>	<b>2019-20</b>
<b>Date of Completion</b>	<b>March, 2022</b>





## **Project-3Repair/Renovation at DIC Office, Srinagar.**

<b><u>Name of Work with</u></b>	<b>Renovation of Corridors of Ground and 1<sup>st</sup> floor at IE BAMK DIC Office Srinagar.</b>
<b>Location</b>	<b>Industrial Estate, BAMK Srinagar</b>
<b>Department/Organization</b>	<b>Director Industries &amp; Commerce, Kashmir</b>
<b>Executive Agency</b>	<b>SICOP</b>
<b>Block/District</b>	<b>District Srinagar</b>
<b>Estimated/Revised Cost (Rs. in Lakhs)</b>	<b>Rs. 11.62 lakh</b>
<b>Total Expenditure incurred (Rs. in Lakhs) on 03/2022</b>	<b>Rs. 11.53 lakh</b>
<b>Project initiation Year</b>	<b>2019-20</b>
<b>Date of Completion</b>	<b>March, 2022</b>
<b>Physical Status</b>	<b>100% complete</b>



